ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Langport-Somerton New Rail Station Indicative Delivery Programme**	915 days	Mon 24/01/22	Fri 25/07/25	
2		Submission of SOBC to RYR	15 days	Mon 24/01/2	Fri 11/02/22	
3		Development of Outline Design (PACE1), Operational Strategy and OBC	131 days	Fri 11/03/22	Fri 09/09/22	2
4		Procurement of Professional consultants to Progress OBC	21 days	Fri 11/03/22	Fri 08/04/22	
5		Update Economic Appraisal	20 days	Mon 11/04/2	Fri 06/05/22	4
6		Development of Outline Design (PACE1), Operational Strategy and OBC	110 days	Mon 11/04/22	Fri 09/09/22	5SS
7		PACE1 Approval Period (Decision to Design)	15 days	Mon 12/09/2	Fri 30/09/22	6
8		Non-Station Planning Approvals (Car Park, Highway Access, Bus/Cycle Infra)	80 days	Mon 09/05/22	Fri 26/08/22	2
9		Non-Station Infra Planning App Preparation	55 days	Mon 09/05/2	Fri 22/07/22	4FS+20 days
10		Non-Station Infra Planning Application Approval	25 days	Mon 25/07/2	Fri 26/08/22	9
11		Non-Station Enabling Site Works (Car Parks, Highway Access)	85 days	Mon 03/10/2	Fri 27/01/23	
12		Site handover from NR	15 days	Mon 03/10/2	Fri 21/10/22	7
13		Site remediation, clearance and construction of site access roads	15 days	Mon 24/10/22	Fri 11/11/22	12
14		Completion of works	55 days	Mon 14/11/2	Fri 27/01/23	13
15		PACE2 Single Option Development	80 days	Mon 02/01/2	Fri 21/04/23	
16		Engagement with NR & Procurement of PACE2 Design Consultant	40 days	Mon 02/01/23	Fri 24/02/23	14FS-20 days
17		Single Option Design Development	40 days	Mon 27/02/2	Fri 21/04/23	16
18		Single Option Development and Design approval (PACE 2)	280 days	Mon 03/04/2	Fri 26/04/24	
19		Station Planning Approvals	94 days	Mon 24/04/2	Thu 31/08/23	
20		Station Planning App Preparation	20 days	Mon 24/04/2	Fri 19/05/23	17
21		Station Planning Application Approval	74 days	Mon 22/05/2	Thu 31/08/23	20
22		FBC (RNEP Decision to Deliver)	65 days	Mon 03/04/2	Fri 30/06/23	
23		Revised Economic Case	45 days	Mon 03/04/2	Fri 02/06/23	20FS-35 days
24		Detailed Management, Commercial and Financial Case	45 days	Mon 03/04/2	Fri 02/06/23	20FS-35 days
25		Full Business Case Submission	20 days	Mon 05/06/2	Fri 30/06/23	24
26		Approval of FBC (RNEP Decision to Deliver)	85 days	Mon 03/07/2	Fri 27/10/23	25
27		Construction Period (Car Parking and Highways Access)	130 days	Mon 30/10/2	Fri 26/04/24	26
28		Pace 3 Detailed Design	130 days	Mon 27/11/2	Fri 24/05/24	
29		Prepare Brief for Design & Build	20 days	Mon 27/11/2	Fri 22/12/23	27SS+20 days
30		PACE3 Procurement of D&B Contractor	20 days	Mon 25/12/2	Fri 19/01/24	29
31		Detailed Design and AFC Drawings	110 days	Mon 25/12/2	Fri 24/05/24	30SS
32		Construction Period (Station)	305 days	Mon 27/05/2	Fri 25/07/25	
33		Construction	260 days	Mon 27/05/2	Fri 23/05/25	31
34		Testing and Commissioning	24 days	Mon 26/05/2	Thu 26/06/25	33
35		New Stopping Services commence at Langport-Somerton	20 days	Mon 30/06/2	Fri 25/07/25	34FS+1 day

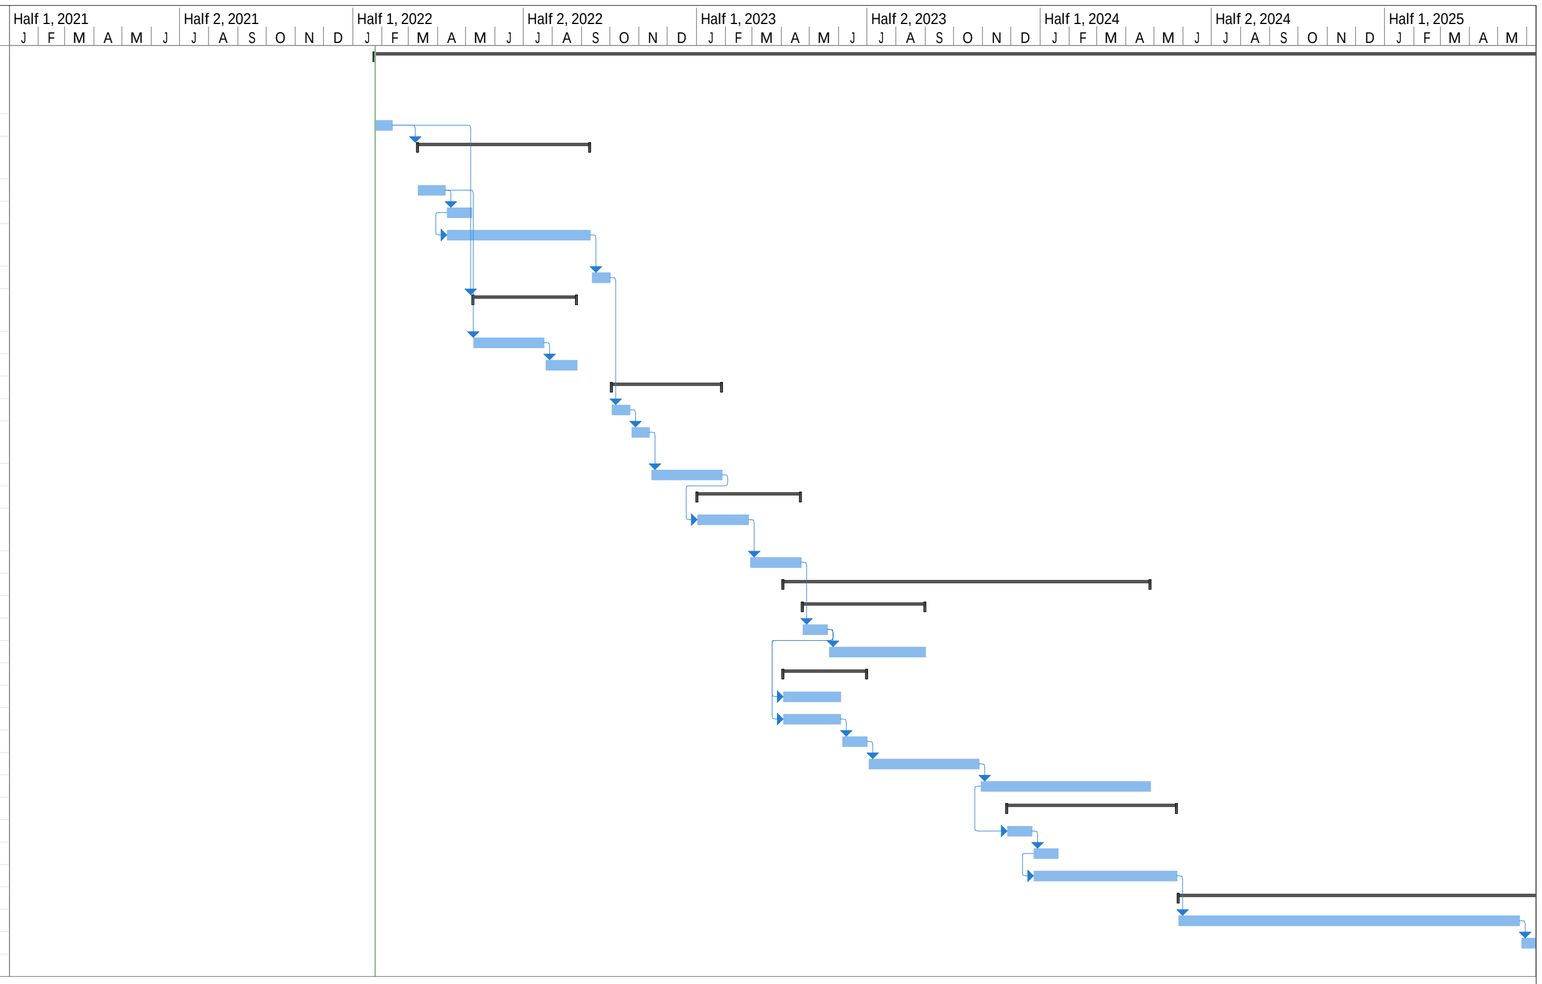

Project: LS Project Delivery Progr
Date: Tue 25/01/22

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Manual Progress		
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline			
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress			
